


Figure 1.2 Annotated Site Drawing Presenting the Construction Activities Conducted at Contract 1 in the Reporting Period

Contract No. YL/2023/01
Hung Shui Kiu / Ha Tsuen New Development Area Second Phase Development – Contract 1 -
Site Formation and Engineering Infrastructure Works

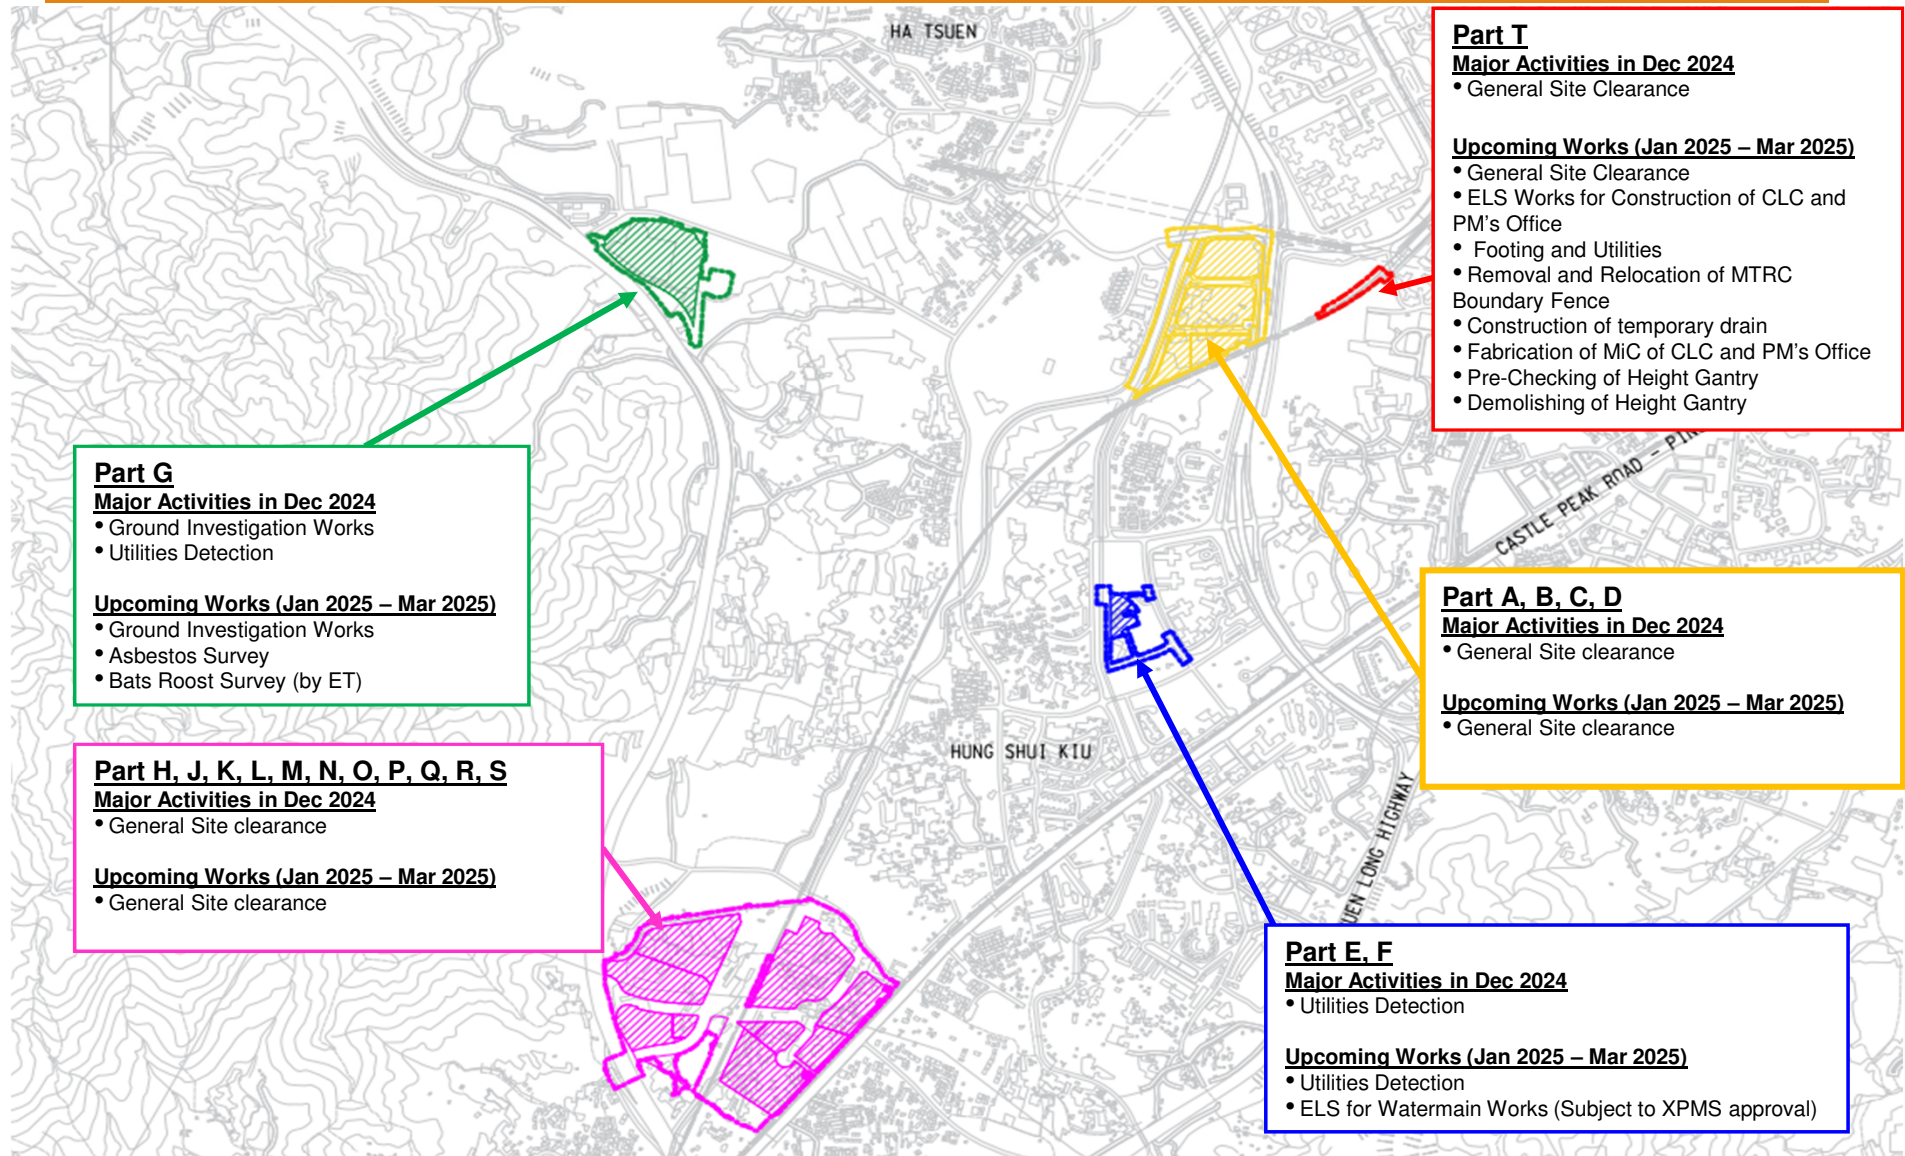

Part G

Major Activities in Dec 2024

- Ground Investigation Works
- Utilities Detection

Upcoming Works (Jan 2025 – Mar 2025)

- Ground Investigation Works
- Asbestos Survey
- Bats Roost Survey (by ET)

Part H, J, K, L, M, N, O, P, Q, R, S

Major Activities in Dec 2024

- General Site clearance

Upcoming Works (Jan 2025 – Mar 2025)

- General Site clearance

Part T

Major Activities in Dec 2024

- General Site Clearance

Upcoming Works (Jan 2025 – Mar 2025)

- General Site Clearance
- ELS Works for Construction of CLC and PM's Office
- Footing and Utilities
- Removal and Relocation of MTRC Boundary Fence
- Construction of temporary drain
- Fabrication of MiC of CLC and PM's Office
- Pre-Checking of Height Gantry
- Demolishing of Height Gantry

Part A, B, C, D

Major Activities in Dec 2024

- General Site clearance

Upcoming Works (Jan 2025 – Mar 2025)

- General Site clearance

Part E, F

Major Activities in Dec 2024

- Utilities Detection

Upcoming Works (Jan 2025 – Mar 2025)

- Utilities Detection
- ELS for Watermain Works (Subject to XPMS approval)
