


Figure 1.3 Annotated Site Drawing Presenting the Construction Activities Conducted at Contract 2 in the Reporting Period

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED.
© OVE ARUP & PARTNERS HONG KONG LIMITED.

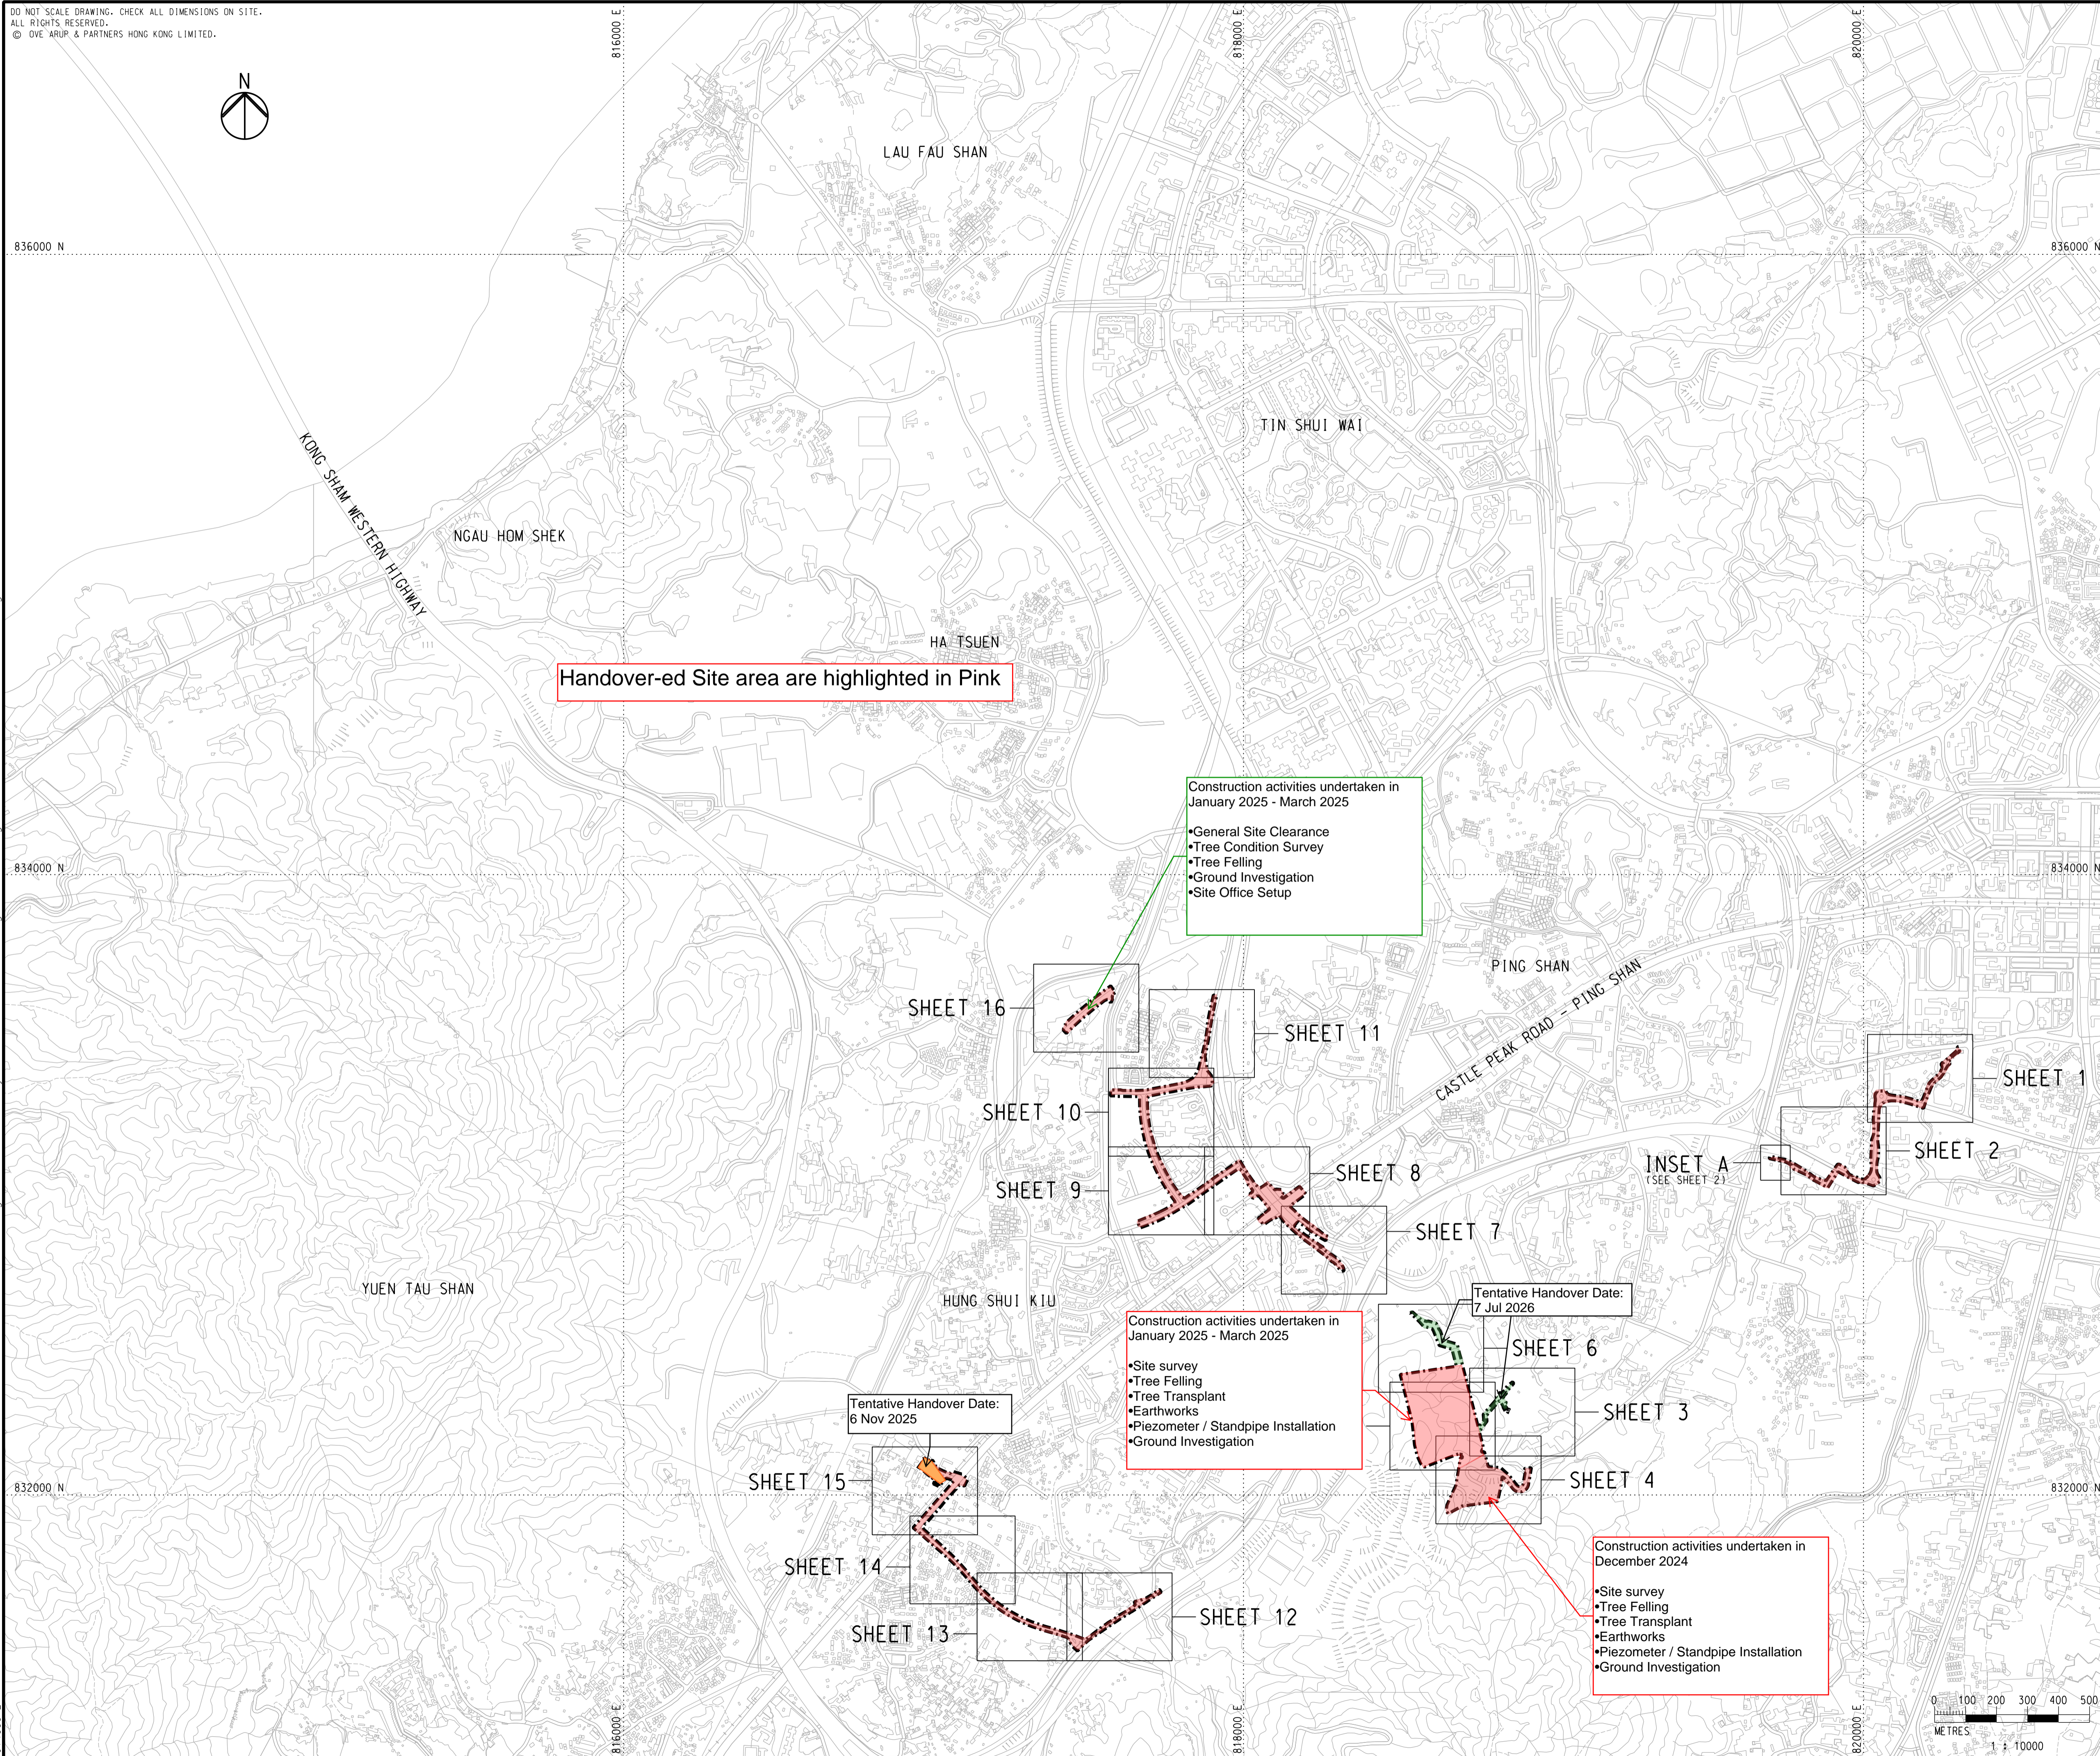

Handover-ed Site area are highlighted in Pink

Construction activities undertaken in January 2025 - March 2025

- General Site Clearance
- Tree Condition Survey
- Tree Felling
- Ground Investigation
- Site Office Setup

Construction activities undertaken in January 2025 - March 2025

- Site survey
- Tree Felling
- Tree Transplant
- Earthworks
- Piezometer / Standpipe Installation
- Ground Investigation

Construction activities undertaken in December 2024

- Site survey
- Tree Felling
- Tree Transplant
- Earthworks
- Piezometer / Standpipe Installation
- Ground Investigation

Tentative Handover Date:
6 Nov 2025

Tentative Handover Date:
7 Jul 2026

LEGEND
--- BOUNDARIES OF THE SITE

00	TENDER ISSUE	DT	08/23
Rev	Description	By	Date

Consultant
ARUP

Project Title
Contract No. YL/2023/02
Hung Shui Kiu/Ha Tsuen
New Development Area
Second Phase Development - Contract 2 -
Fresh Water Service Reservoir and
Associated Mainlaying Works

Drawing title
OVERALL LAYOUT PLAN

Drawing no. 282748/C2/GEN/1100		Rev. 00	
Drawn MAN	Date 05/23	Checked	Approved DVC
Scale 1:10000 @ A1		Status TENDER	

COPYRIGHT RESERVED



土木工程拓展署
Civil Engineering and
Development Department

Printed by : reman.yick
File name : J:\282000\282748-00_CE_71-2020_HSK-HT_NDA-DC_Package B\05_Int_Proj_Data\05_89_Drafting\02-Drawing\Civil\282748_C2_GEN_1100.dgn
Date : 9/26/2023

